TEST REPORT

Date:_____
Session: 2

1. BREAKER DATA

Station:	Line/Compartment:
Breaker ID:	Serial number:
Manufacturer:	Breaker type:

2. TEST DATA

Type of test:	Operator:
Company name:	Reference:

3. COMMENTS

4. GENERAL TEST CONDITIONS

Sequence: CO		
Measuring time: 1s		Time base: seconds
Pulse	Length	Delay
Open	0.29s	0.01s
Close	0.10s	
Open		

5. MOTION TEST CONDITIONS

Nominal stroke length: 100.0mm

Closing speed calculation points

Upper point: at close of main contact
Lower point: 10.0ms before upper point

Opening speed calculation points

Upper point: at open of main contact
Lower point: 10.0ms after upper point

6. TIMING RESULTS

L1,L2,L3: Phase 1,2 and 3, Main contacts
X1,X2: Auxiliary contact 1 and 2
Presented events:
Initial contact touch at closure and final contact separation at opening
Opening bounces < 10ms are suppressed

L1	L2	L3
151.0ms Close 216.1ms Open	151.4ms Close 214.7ms Open	151.5ms Close 215.4ms Open

X1	X2

Timing calculations

Parameter/Phase	L1	L2	L3
Closing Time	151.0ms	151.4ms	151.5ms
Opening Time	216.1ms	214.7ms	215.4ms
Time C-O (On time)	64.6ms		

Difference between phases

Closing Time	0.5ms
Opening Time	1.4ms

7. MOTION RESULTS

Parameter/Phase	L1	L2	L3
Closing speed	------		
Opening speed	0.1m/s		
Stroke	95.6mm		

8. GRAPH
L1,L2,L3: Phase 1,2 and 3, Main contacts
X1,X2: Auxiliary contact 1 and 2
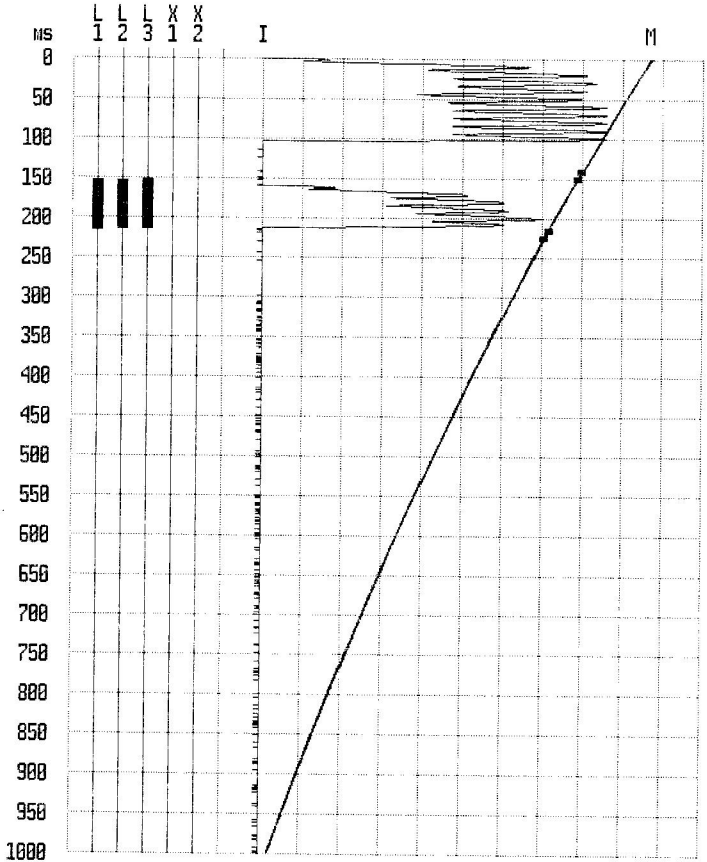
I: Current	-200mA	Scale:200mA/d	2.200A
M: Motion	0.0mm	Scale:10mm/d	120.0mm
